


# WHITE HALL DAM - COMPLETED

## DATA

**Watershed:** Gunpowder  
**Stream:** Little Falls, Tributary to Big Falls  
**Stream Order:** 4<sup>th</sup> Order  
**County:** Baltimore County  
**Location:** Weisburg Ave, Near White Hall MD  
**Lat/Long:** N39\*37.290' W076\*37.817'  
**Cong. District:** MD 06  
**Ownership:** Private  
**Point of Contact:** Jim Thompson - DNR  
**Structure Type:** Concrete Dam  
**Type of Passage:** Removal/Bypass  
**Miles Reopened:** 16 miles.  
**Target Species:** Brown Trout, Rainbow Trout  
**Start / Finish Date:** Fall/Winter 2010

## PROJECT BUDGET

Project Partner	Design	Construction
<b>Estimated Cost</b>	<b>\$85K</b>	<b>\$221,866</b>
FAF/CBT		\$30,500
NRCS	\$87,396	\$159,077
DNR Fisheries		\$35,000
FWS		\$7,391/\$1,800
<b>Total</b>	<b>\$87,396</b>	<b>\$198,768</b>
Codes: (S)-Secured, (A)-Applied		

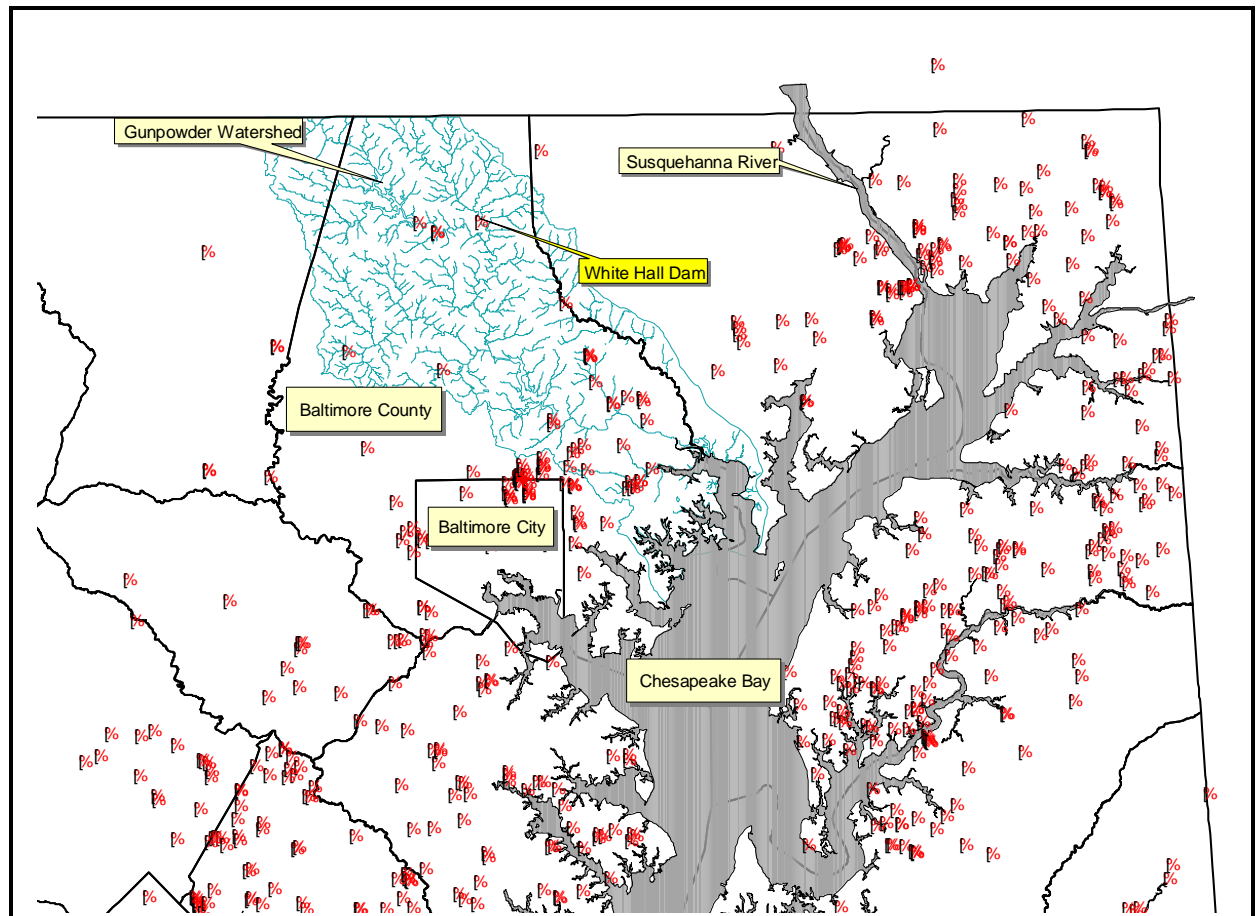

## COMMENTS

**LAST UPDATED – 12/05/2011**

The Whitehall Dam was removed in August of 2011 providing passage to wild reproducing brown trout and alleviating thermal pollution impacts. Hurricane Irene and Tropical Storm Lee caused significant damage to the project site in late August. Fortunately the National Resources Conservation Service (NRCS) secured last-minute funding to repair the structures and regrade the banks.

## PROJECT PICTURES



**BEFORE**



**AFTER**
